

400 North IMPROVED

Bountiful

S.R. 106 (400 North) in Bountiful; 800 West to Main Street


400 North Improved Project Update- July 21, 2016

The Utah Department of Transportation (UDOT) is resurfacing S.R. 106 (400 North) in Bountiful from 800 West to Main Street to increase the life the roadway.

Construction Activities for July 21- July 28, 2016

*email updates sent as schedule changes

Traffic has now been shifted from Main Street to 500 West. Another traffic shift is scheduled for early August. Traffic shift configuration below.

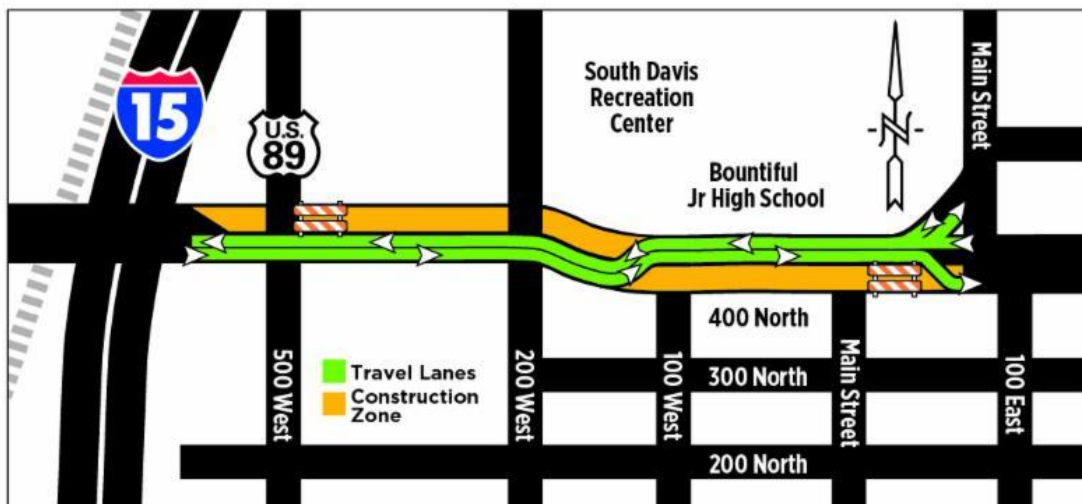

BUSINESSES ARE STILL OPEN DURING CONSTRUCTION!!!

Don't forget to support local businesses on 400 North.

400 North- Main Street to 500 West (Phase 1): Work is ongoing on the north side of the street, starting at Main Street and moving west towards I-15 through July.

This week:

- Crews poured concrete on driveway approaches between 200 West to 17 East Main Street last week. Concrete is curing, and residents will be notified when driveway accesses are available.
 - Curb and gutter is scheduled to be poured as early as July 28th. Driveway approaches will follow.

- In early August, crews are scheduled to finish pouring concrete from 200 West to 500 West. With curb and gutter concrete work following.
 - Residents are asked to park at an alternate location for up to 10 days for each pouring activity and to allow concrete to cure.
- In mid-August, crews are scheduled to shift traffic from 200 West to 500 West to the north side of 400 North.

400 North- 500 West to I-15 (Phase 2):

Work during this phase will begin on the south side of 400 North and move from east to west.

- Crews have begun excavating and milling activities on the south side of 400 North from Main Street to 200 West.
- In late July crews will begin hauling and placing materials in preparation for concrete work in early August.
 - Residents can expect an increase in heavy truck traffic and noise.
 - Concrete pouring is expected to begin late July and will occur at night. Driveways in this segment will be closed for approximately 10 days while the concrete cures. Please begin making preparations to park in an alternate location.

400 North- West of I-15 to 800 West (Phase 3):

Work during this phase will begin east of 800 West and 400 North and move towards the west side of 500 West. During this work, intermittent, single lane traffic from I-15 to 800 West is anticipated.

- Milling activities are anticipated to occur in late July beginning at I-15 and heading west on the north side of 400 North.
- Concrete paving work is scheduled to follow in early to mid-August.
 - Residents can expect to park in an alternate location while concrete cures.
 - Expect congestion and traffic delays of up to ten minutes.
- Crews are scheduled to shift traffic in early August between I-15 and 800 West on the north side of 400 North in preparation for milling activities to begin on the south side of 400 North.

Project Description:

The project will reconstruct the roadway in concrete for a longer pavement life and less future maintenance. Additionally, the project will:

- Add new curb, gutter, and some sidewalk and driveway approaches from 500 West to Main Street.
- Add radar detection at the 400 North/200 West intersection to improve traffic flow.

Project Impacts:

- 400 North reduced to one lane in each direction between Main Street and 500 West.
- Motorists should be prepared for significant delays and use alternate routes when possible.
- Area residents and businesses can expect short-term intermittent driveway interruptions.
- Surrounding residents and businesses can expect traffic restrictions, construction equipment and vehicles, and an increase in noise during the day and at night.

- Motorists can reduce delays by using alternate routes, avoiding peak travel times, telecommuting, carpooling or combining trips.
- Pedestrians should be alert and follow posted signs. It is recommended that an alternate route be used.
- Through the duration of this project, trash pick-up days have been changed to every Friday between 9 a.m. to 1 p.m. for the entire corridor. To maintain trash removal while work continues, crews will move trash bins to the other side of the street every Friday morning at 8 a.m. To ensure bins are moved, residents must place their bins on the sidewalk by 6 p.m. the evening prior.

Project Timeline:

Construction began in mid May and is scheduled to continue through October 2016. This aggressive construction schedule was designed to work around the Bountiful City water line and irrigation project currently underway and complete work in one construction season. Please see below graphic for project timelines and phasing.



Project Contact Information:

This project has a dedicated public information team to work with area residents and stakeholders. Please feel free to contact us about this project. We are here to help! Updated information is available at www.udot.utah.gov/go/400north, by emailing 400North@utah.gov, or calling the project hotline at **888-556-0232**, ext 2.
