

US 89

Preservation

1000 N to Eagle Ridge Drive

August 16, 2017

Current Work

The bulk of the project is now complete, with crews finishing up micro-surfacing and the first pass of re-striping. After the asphalt surface has adequately cured, a second coat of lane striping will be painted.

A street sweeper will soon be coming through the project corridor. Construction crews will continue to work overnight to lay any remaining pavement markings such as turn arrows and crosswalk bars. To accomplish this task, single lane closures will be required during the hours of 7:00 p.m. to 7:00 a.m.



Microsurfacing work along US-89 from Eagle Ridge Drive to the I-15 connection is complete.

These closures will likely be at major intersections and closures will be in place for approximately one hour. These temporary closures may cause minor delays and congestion to occur.

A total of 91 pedestrian ramps have been upgraded to current standards, and finishing touches such as landscaping are underway. Work on sign replacement will take place through the end of the week.

Traffic Alerts

Impacts to the following areas are anticipated.


US-89 Eagle Ridge Drive north to I-15 entrance

- Overnight single lane closures may be in place (between 7 p.m. and 7 a.m.)
- Traffic control devices may be in place
- Temporary and intermittent closures of right and left turns, median and driveway access may be in place
- Delays and congestion are possible

What can I expect during construction?

Project impacts may include:

- Sidewalk closures
- Noise, dust, vibrations
- Some right-hand turn lanes on US-89 may be temporarily closed
- Some driveways may have access impacted while work takes place
- Minor traffic delays, lane shifts and lane closures on US-89 during overnight hours

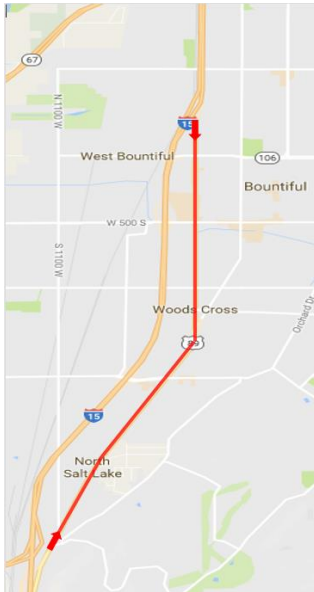

Project Overview

UDOT will be performing asphalt maintenance on a four mile corridor on US-89 through Bountiful, West Bountiful, Woods Cross and North Salt Lake (from Eagle Ridge Drive to 1000 North/I-15). The pavement will receive a micro-surface treatment, which will extend the life of the asphalt.

The project will also be upgrading approximately 100 sidewalk pedestrian ramps to become compliant with federal Americans With Disabilities Act (ADA) standards.

Work on pedestrian ramps began at the south end of the project limits, and crews plan to work their way north. Construction work is scheduled for completion by the end of August.

Contact Us:

For the most current traffic information, visit the UDOT Traffic website, udottraffic.utah.gov, or download the UDOT Traffic App for your iOS or Android device.

UDOT and our Public Involvement Team are here to work with you and keep you informed! For questions or concerns please call or email us. For weekly email updates, send an email with "updates" in the subject line to: US89BountifulRepave@utah.gov.

Hotline: 1-800-945-2744

E-mail: US89BountifulRepave@utah.gov

Website: udot.utah.gov/go/us89bountifulrepave
